


Start date	06APR09
Finish date	29APR11
Data date	08OCT09
Run date	11OCT09
Page number	1A
© Primavera Systems, Inc.	

**Lease Crutcher Lewis
Lynnwood Recreation Center**

- Early bar
- Progress bar
- Critical bar
- Summary bar
- Start milestone point
- Finish milestone point

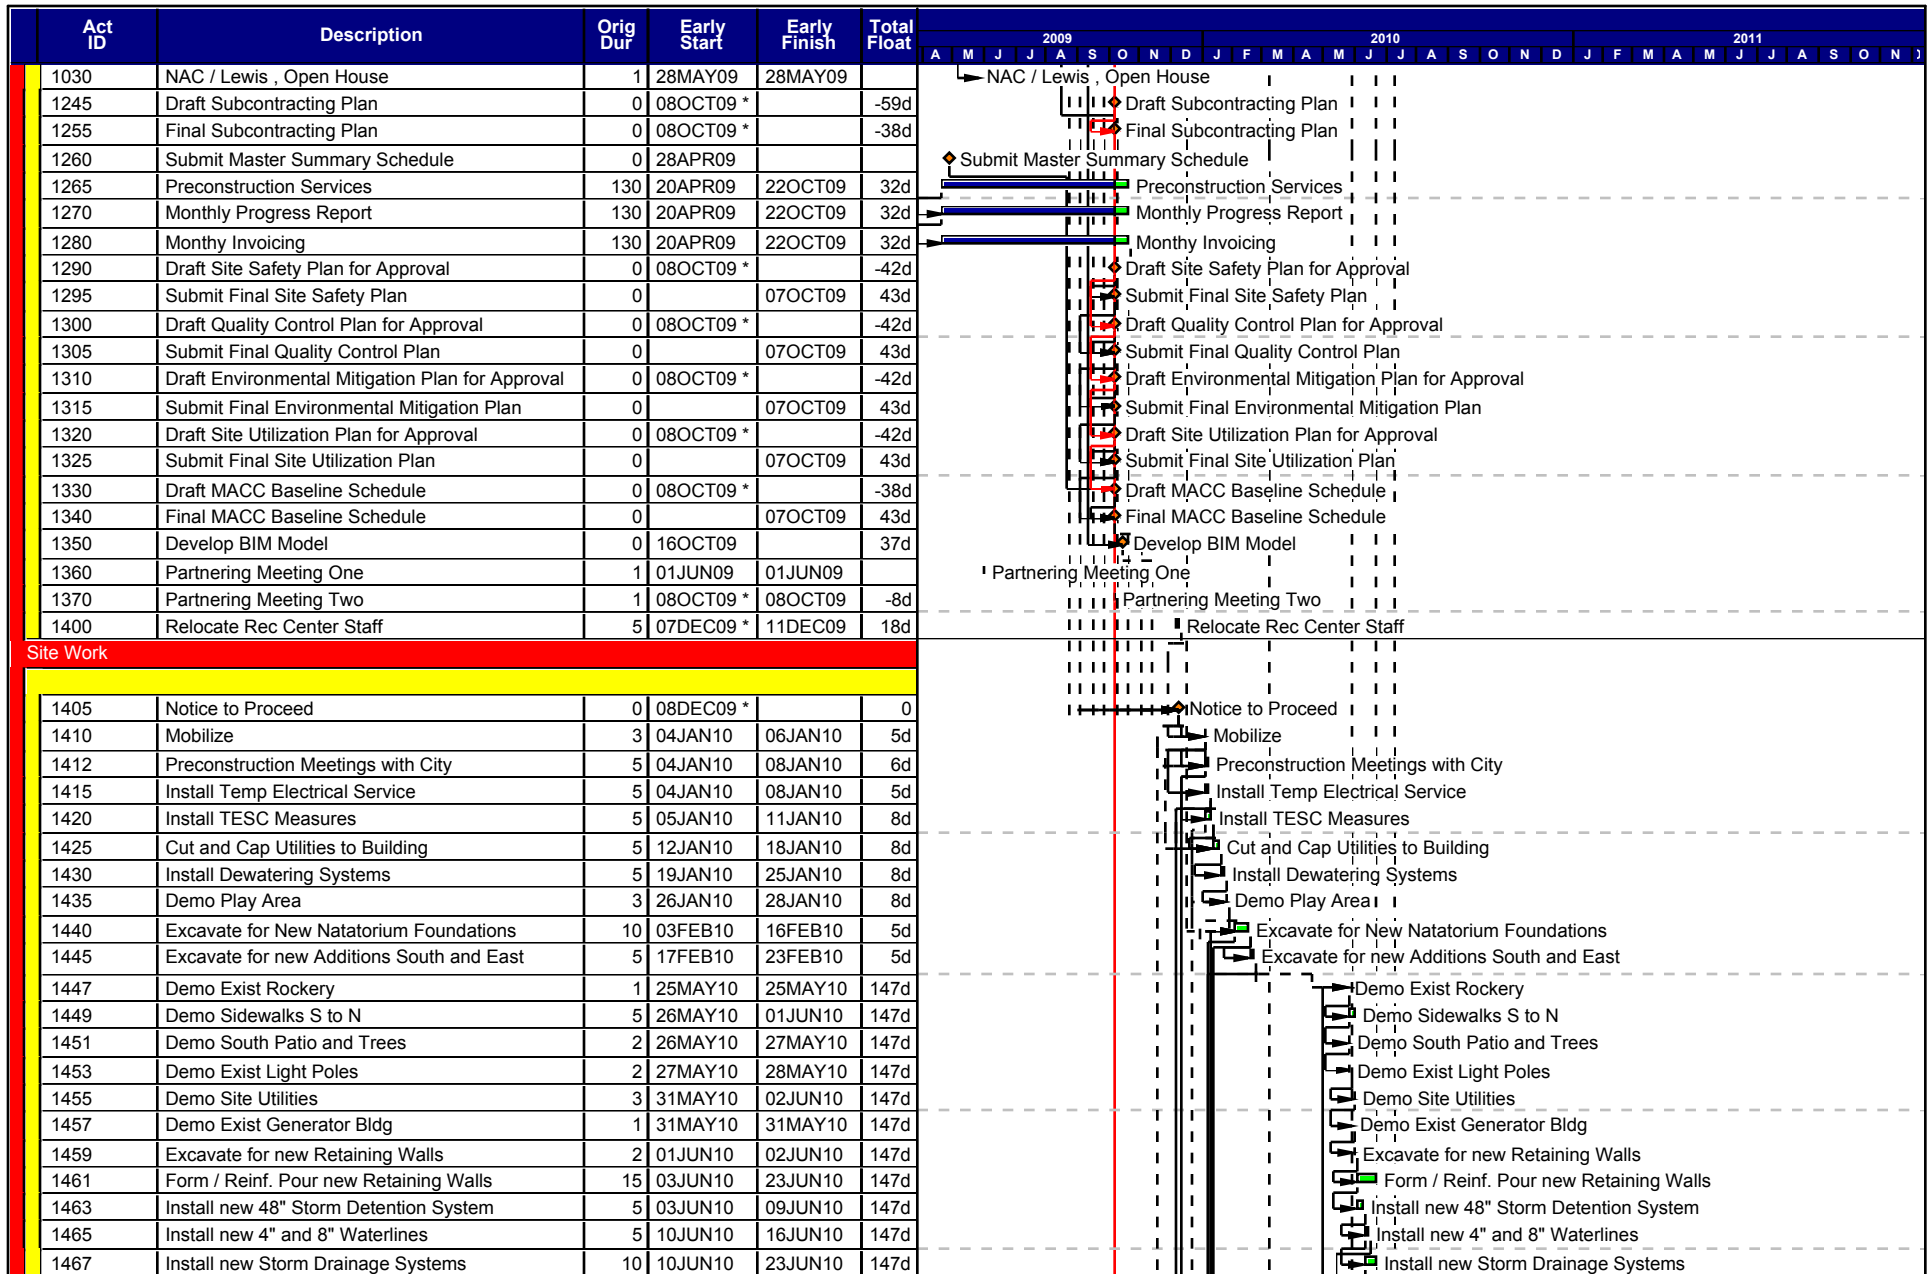

Start date	06APR09
Finish date	29APR11
Data date	08OCT09
Run date	11OCT09
Page number	2A
© Primavera Systems, Inc.	

**Lease Crutcher Lewis
Lynnwood Recreation Center**

- █ Early bar
- █ Progress bar
- █ Critical bar
- █ Summary bar
- ◆ Start milestone point
- ◆ Finish milestone point

Act ID	Description	Orig Dur	Early Start	Early Finish	Total Float	2009												2010												2011											
						A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N				
Commissioning / Close out																																									
1240	Start up / Commission Mechanical Systems	60	12OCT10	03JAN11	19d																																				
1250	Commission Pools / Equipment	60	23DEC10	16MAR11	17d																																				
3020	Punch list	30	04JAN11	14FEB11	59d																																				
3030	Final Inspections	5	04JAN11	10JAN11	5d																																				
3080	Substantial Completion	0		03JAN11	5d																																				
3090	Final Completion	0		01APR11	5d																																				
3095	TCO	0		10JAN11	5d																																				
3100	Owner Move in	10	21MAR11	01APR11	5d																																				
3110	Grand Opening	0		29APR11	5d																																				

Start date 06APR09
 Finish date 29APR11
 Data date 08OCT09
 Run date 11OCT09
 Page number 5A
 © Primavera Systems, Inc.

**Lease Crutcher Lewis
 Lynnwood Recreation Center**

- Early bar
- Progress bar
- Critical bar
- Summary bar
- Start milestone point
- Finish milestone point
